NOTES:
SPECIAL NOTES

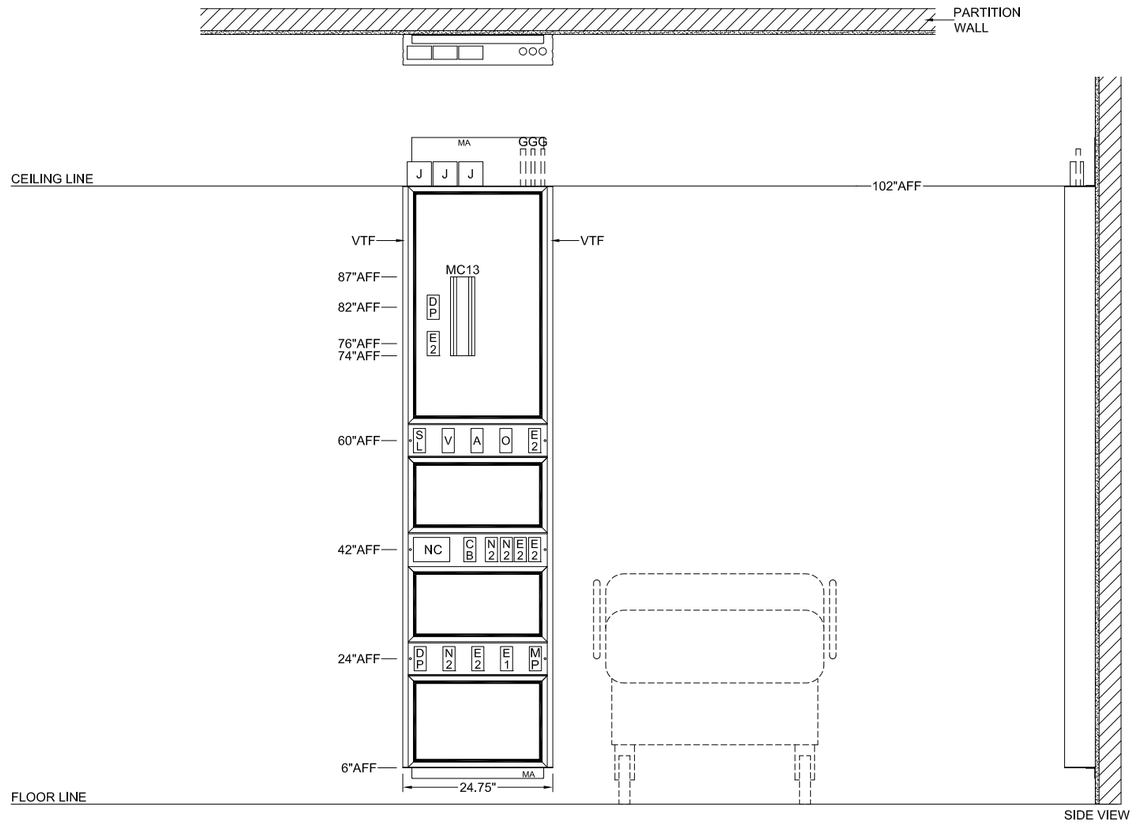

GENERAL SPECIFICATIONS:

ELECTRICAL		PLUMBING		FINISHES			
NORMAL POWER JUNCTION BOX:	J1	COPPER TUBING TYPE:	L	LAMINATE: L1			
EMERGENCY POWER JUNCTION BOX:	J2	OXYGEN SIZE (I.D.):	1/2"	TYPE:	LAMINATE BRAND:	LAMINATE COLOR:	GRAIN ORIENTATION:
LOW VOLTAGE JUNCTION BOX:	J3	MEDICAL AIR SIZE (I.D.):	1/2"	-	-	-	-
		VACUUM SIZE (I.D.):	3/4"				
CONDUIT SIZE; LINE VOLTAGE:	1/2"						
CONDUIT SIZE; LOW VOLTAGE:	3/4"						
CONDUIT CONNECTORS:	STD. SET SCREW						
WIRE TYPE:	THHN, STRANDED			ELECTRICAL COVER PLATES:	SURF OR PLATINUM GRAY		
WIRE SIZE:	12 AWG			EQUIPMENT MANAGEMENT:	ANODIZED ALUMINUM		
GROUND WIRE COLOR:	GREEN			UNIT TRIM:	ANODIZED ALUMINUM		

LEGEND:

REQ	SYM	DESCRIPTION	REQ	SYM	DESCRIPTION
1	O	OXYGEN OUTLET	2	DP	DATA OUTLET PROVISION
1	A	AIR OUTLET	1	MC13	MONITOR CHANNEL ONLY, 13" LENGTH
1	V	VACUUM OUTLET	2	VTF	VERTICAL EQUIPMENT MOUNTING TRACK, FASCIA
1	SL	VACUUM BOTTLE SLIDE	2	MA	MOUNTING ANGLE OR BRACKET
3	N2	DUPLEX RECEPTACLE, 8300 IVORY 20A, 125V, H.G., NORMAL POWER			
1	E1	SINGLE RECEPTACLE, 8310 RED, 20A, 125V, H.G., EMER. POWER			
5	E2	DUPLEX RECEPTACLE, 8300 RED 20A, 125V, H.G., EMER. POWER			
1	NC	NURSE CALL PROVISION			
1	CB	CODE BLUE PROVISION			
1	MP	MULTI-PIN BED RECEPT. PROVISION			

ACCESSORIES NOT SHOWN (PER UNIT)

REQ	DESCRIPTION

MODULAR SERVICES COMPANY®
500 EAST BRITTON ROAD
OKLAHOMA CITY, OK 73114
www.modularservices.com

PROJECT
HOSPITAL
PROJECT
CITY, STATE

TOTAL QTY:	FLATWALL UNIT MODEL #1113	
X		
AS SHOWN: X	DRAWN BY: XXX	DRAWING # 4XXXX
OPPOSITE: X	DATE: XX/XX/XX	PROJECT #: XXXX / SALES ORDER #: XXXXX
